

[Subscribe](#)[Past Issues](#)[Translate](#) ▼[News on the Germany Beck Project](#)[View this email in your browser](#)

# Germany Beck Project

## Weeks 60 & 61 commencing Monday 31st July 2017

This is the 31st edition of the newsletter that keeps you up to date with the progress of the Germany Beck junction works on the A19 in Fulford.

The water main diversion on the A19 is now complete. A medium pressure gas main diversion has been delayed and has hence resulted in a break in the use of temporary traffic lights on the A19.

The brickwork walls to the top of the sheet piled retaining walls have continued, along with the construction of the footpaths to the east of Fordlands Road.




During the next 2 weeks we will be -

[Subscribe](#)
[Past Issues](#)

- Continuing installation of the elliptical drainage pipes within the spine road embankment.

The closure of the eastern footpath on the A19 remains in place.

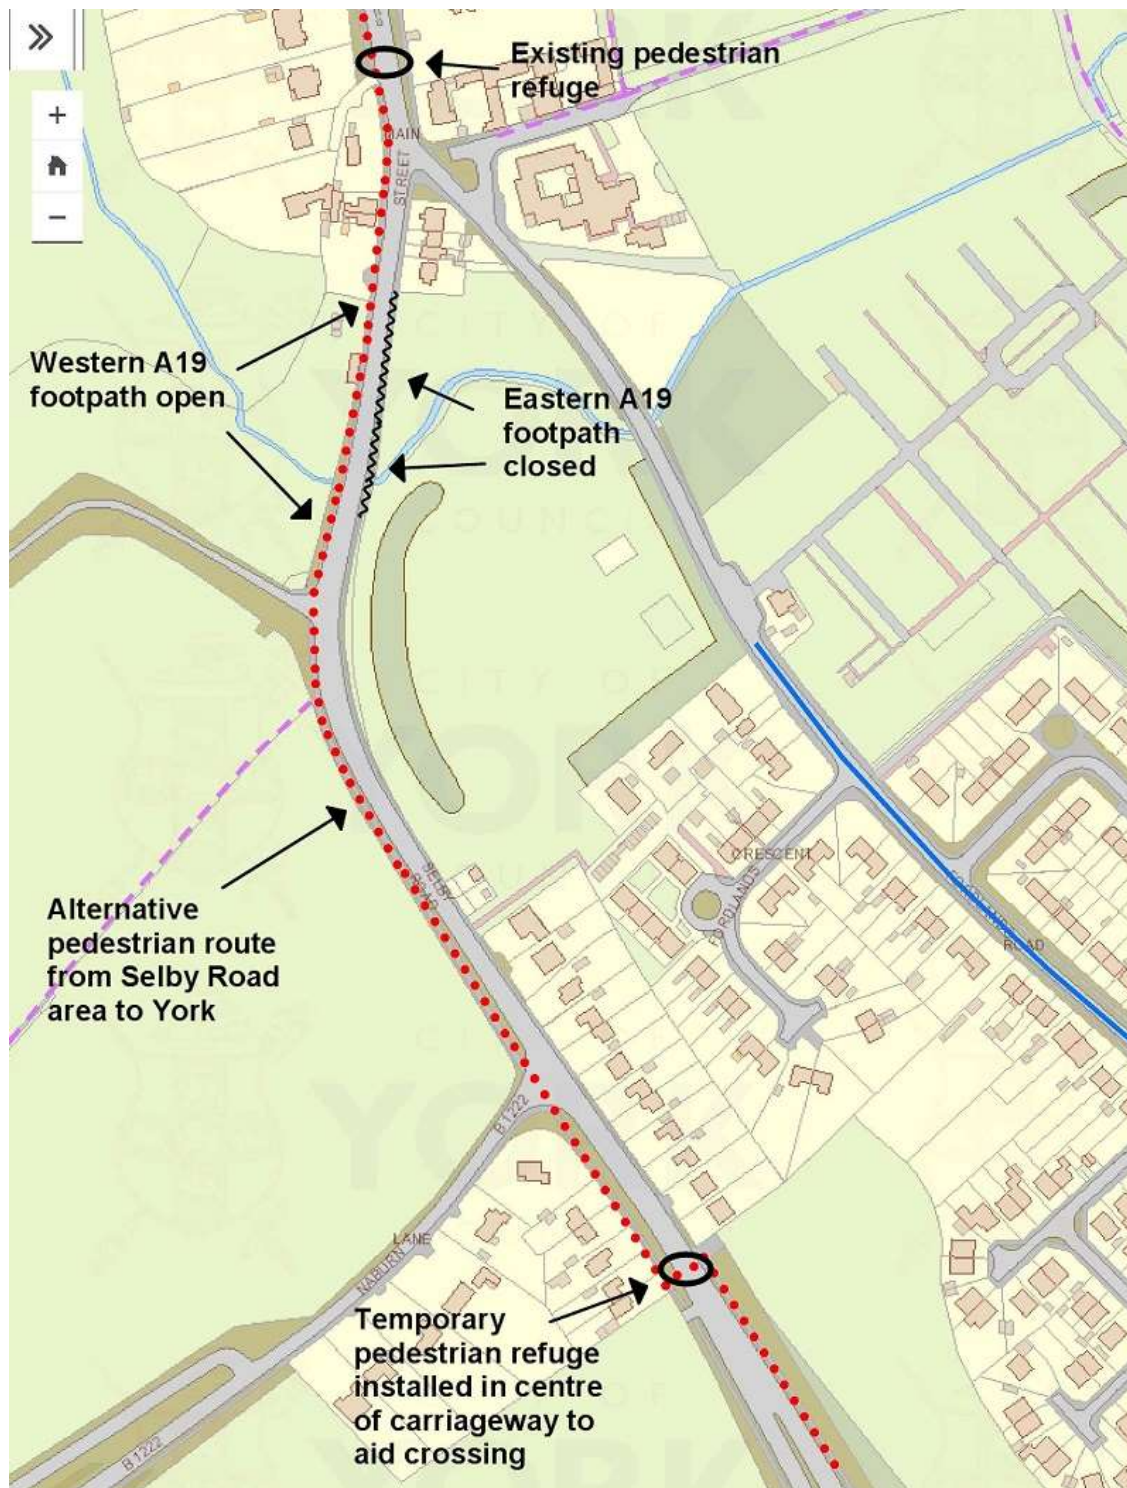

## Safety for children and the wider public.

Please be assured that the different areas of works will be securely fenced at all times to ensure the safety of the public.

We will be receiving deliveries to site this week. Each delivery will be guided into site by one of our

[Subscribe](#)[Past Issues](#)

Pedestrians will be given right of way along the footpaths of Fordlands Road but please be aware of deliveries using the entrances to site off Fordlands Road on occasion.

Previous editions of our newsletters can be accessed on our website [here](#)

*Copyright © 2017 Howard Civil Engineering, All rights reserved.*

Want to change how you receive these emails?  
You can [update your preferences](#) or [unsubscribe from this list](#)

The MailChimp logo is displayed in a white, cursive font within a grey rounded rectangular box.
