

[Subscribe](#)[Share ▼](#)[Past Issues](#)[Translate ▼](#)[News on the Germany Beck Project](#)[View this email in your browser](#)

# Germany Beck Project

## Weeks 35 & 36 commencing 6th February 2017

This is the 18th edition of the newsletter that keeps you up to date with the progress of the Germany Beck junction works on the A19 in Fulford.

During the last week we have been removing some tree stumps adjacent to the A19 which will allow us to complete the sheet piled wall. We have also been preparing for the concrete works which form part of the retaining wall structure.

The works at Germany Beck will step up a gear next week with the piling rig returning to site.

The piling rig is due to come to site on Monday 6th February. It will be delivered on several large low loaders. The low loaders have been given official permission by the CYC Traffic Project Officer to turn right into Fordlands Road from the A19 after safely stopping the traffic for a short period. They have been advised to avoid the peak hours of 7.30am to 9.30am.

The piling works will commence on Monday 6th or Tuesday 7th. A period of 'pre-augering' (loosening the soils with a long drill to allow easier piling) will take place for 3 to 4 days before the driving of piles commences towards the end of the week. It is expected that the piling contractor will be on site for a total period of 2 to 3 weeks

The eastern footpath of the A19 will now remain closed for several weeks.


Subscribe

Share

Past Issues

Existing pedestrian

Translate

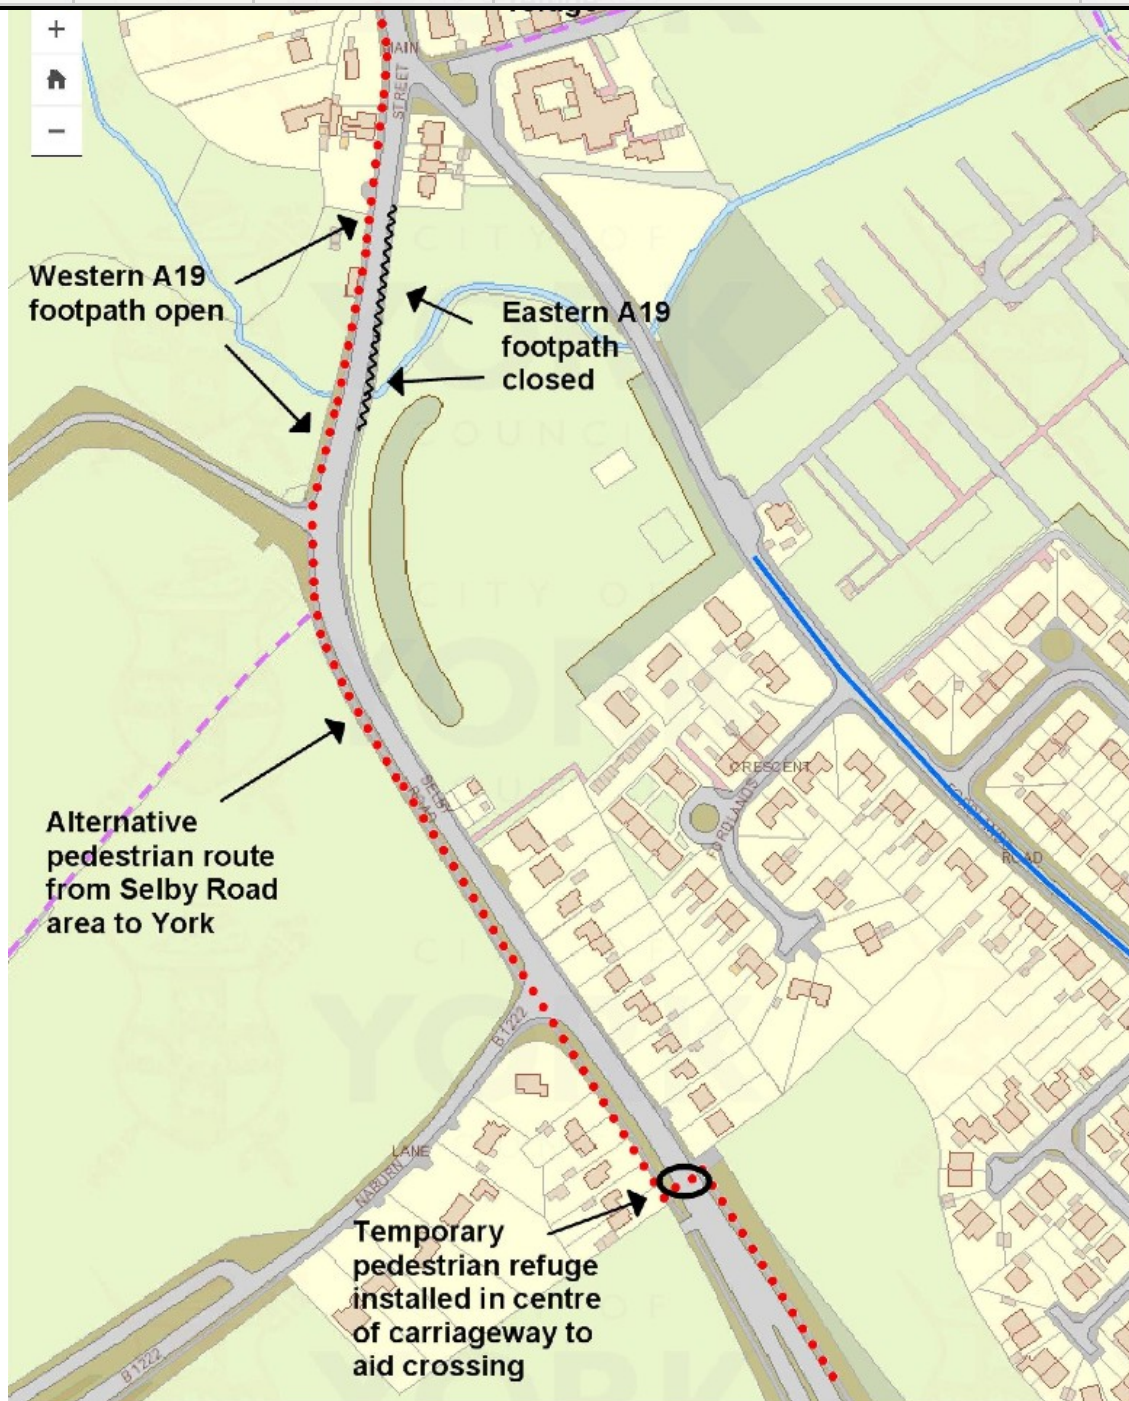


## WARNING - USE OF TEMPORARY TRAFFIC LIGHTS ON THE A19

As advised in the previous newsletter, in order to complete the piling works we need to install temporary traffic lights on the A19. We need to locate the piling rig on the southbound A19 carriageway to install the section of sheet piled wall closest to the A19.

From Wednesday 8th the temporary lights will operate on week days, during 'off peak' hours only, from 9.30 until 3.30pm. This is likely to cause disruption to traffic using the A19. The lights will be in operation for 2 to 3 weeks.

your journeys, especially those collecting children from schools at the end of the day. Fordlands Road will remain open at all times but is also likely to be affected with disruption to traffic

The diagram below shows where the lights will be set up. We apologise for the inconvenience this will cause.

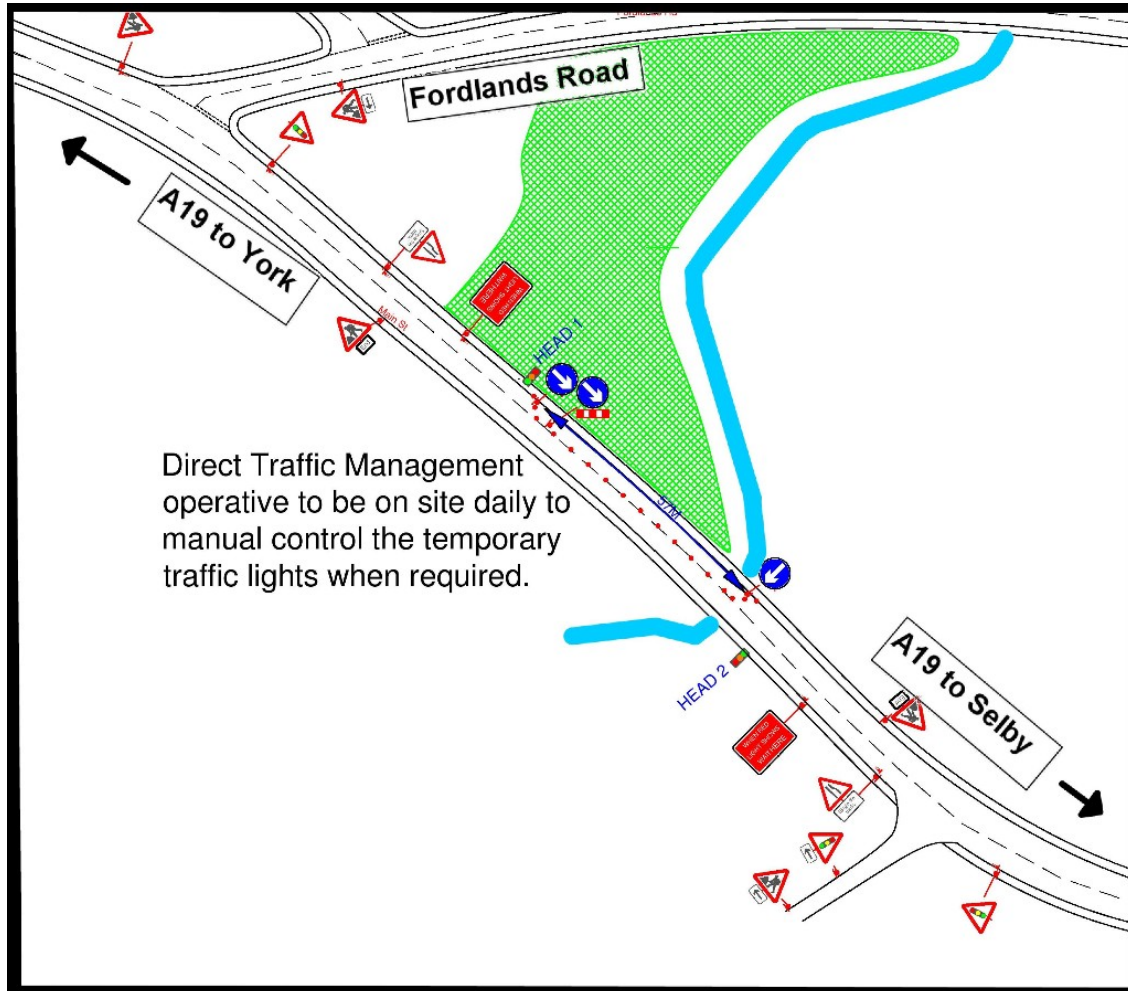

## Safety for children and the wider public.

Please be assured that the different areas of works will be securely fenced at all times to ensure the safety of the public.

We will be receiving deliveries to site this week. Each delivery will be guided into site by one of our employees once traffic and pedestrians are clear from the site entrance. Please be patient if you are held up for a short time whilst these manoeuvres take place.

Pedestrians will be given right of way along the footpaths of Fordlands Road but please be aware of deliveries using the entrances to site off Fordlands Road on occasion.

Previous editions of our newsletters can be accessed on our website [here](#)

<a href="#">Subscribe</a>	<a href="#">Share ▼</a>	<a href="#">Past Issues</a>	<a href="#">Translate ▼</a>
---------------------------	-------------------------	-----------------------------	-----------------------------

Copyright © 2017 Howard Civil Engineering. All rights reserved.

Want to change how you receive these emails?  
You can [update your preferences](#) or [unsubscribe from this list](#)

