

[Subscribe](#)[Share ▼](#)[Past Issues](#)[Translate ▼](#)[News on the Germany Beck Project](#)[View this email in your browser](#)

Germany Beck Project

Weeks 28,29 & 30 commencing 19th December

This is the fifteenth edition of the newsletter that keeps you up to date with the progress of the Germany Beck junction works on the A19 in Fulford. Works on site will cease between Christmas and the New Year, therefore this newsletter also covers the first week in January.

During the past 2 weeks we have been progressing with the drainage to the east and the west of Fordlands Road. The images below show the installation of a 450mm diameter pipe being installed, together with the concrete headwalls at either side of the embankment.

Next week we will be carrying out some trial holes in the grassed area to the west of the A19 to confirm the position some services to the rear of the footpath.



[Subscribe](#)[Share ▼](#)[Past Issues](#)[Translate ▼](#)

As a notice of clearance piling in the vicinity of the Germany Beck culvert are now scheduled for the New Year. The daily footpath closure as described below will not come into force until we return to site in January.

As per the previous newsletter in order gain access to the tree stumps we need to remove to complete the piling works adjacent to the Germany Beck A19 culvert we will be closing the footpath that runs along the east of the A19 between the hours of 9am and 3pm for a period of approximately 5 days. Having monitored the number of pedestrians using the footpath between those hours we know that this should not inconvenience many. However signs will be erected on Selby Road and Main Street to advise you of the footpath closure and a temporary pedestrian island will be installed at a point on Selby Road, as agreed by CYC, to aid those wishing to cross the A19 during those times.

You will also see traffic cones placed on the A19 which will reduce the width of the A19 slightly adjacent to the site. This is to provide our operatives with a safety zone between themselves and the traffic during the stump clearance works. Two way traffic will be maintained at all times.


Subscribe

Share

Past Issues

Existing pedestrian

Translate

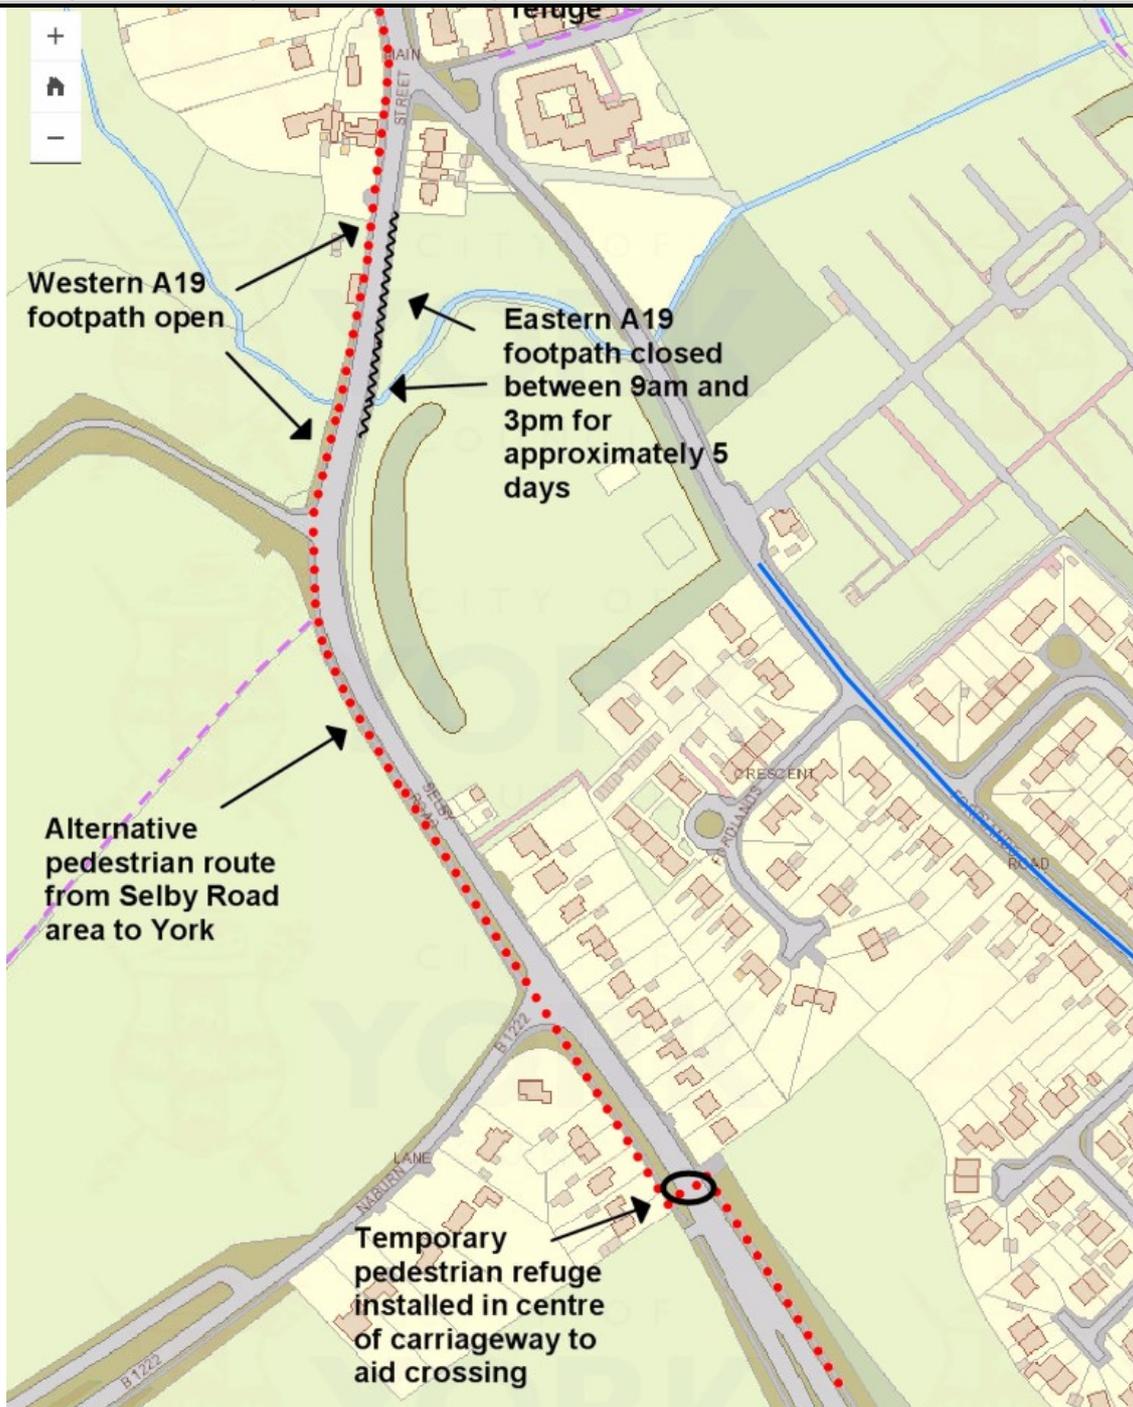

Christmas Shutdown Friday 23rd December - Tuesday 3rd January.

The site will be shut down between Christmas and the New Year although visits will be made daily by one of our employees over the Christmas break to make safety and security checks.

In the event that you wish to report anything regarding the site in general please make contact with our Project Manager Wayne McCutcheon on 07793 244495. Please leave him a message if he does not pick up immediately.

[Subscribe](#)[Share](#) ▼[Past Issues](#)[Translate](#) ▼

Please be assured that the different areas of works will be securely fenced at all times to ensure the safety of the public.

We will be receiving few deliveries to site this week. Each delivery will be guided into site by one of our employees once traffic and pedestrians are clear from the site entrance. Please be patient if you are held up for a short time whilst these manoeuvres take place.

Pedestrians will be given right of way along the footpaths of Fordlands Road but please be aware of deliveries using the entrances to site off Fordlands Road on occasion.

Previous editions of our newsletters can be accessed on our website [here](#)

Copyright © 2016 Howard Civil Engineering, All rights reserved.

Want to change how you receive these emails?
You can [update your preferences](#) or [unsubscribe from this list](#)

MailChimp
