

News on the Germany Beck Project

[View this email in your browser](#)



# Germany Beck Project

## Weeks 82 & 83 commencing Monday 8th January 2018

This is the 42nd edition of the newsletter that keeps you up to date with the progress of the Germany Beck junction works on the A19 in Fulford.

After overcoming various challenges the piling in the A19 to support the culvert protection structure is now complete, enabling us to now proceed with the culvert protection works in this area.

We have been continuing the construction of the realigned footpath to the south of the Beck and have also progressed the public footpaths in the flood alleviation area.

The brickwork parapets continue.



During the next 2 weeks we will be -

- Continuing the brickwork walls to the top of the sheet piled retaining structure
- Installing ducts across the A19 for the future traffic signals and power cable diversions.
- Commencing work to the culvert protection structure
- Installing ducts and foundations for the new street lighting in the Fulford Road area

[Subscribe](#)[Past Issues](#)[Install ducts and chambers for the new traffic signals](#)

The closure of the eastern footpath on the A19 remains in place.


## **OFF PEAK TRAFFIC LIGHTS ON A19 UNTIL 12th JANUARY.**

A historical culvert is located under the A19. We need to protect the culvert from any possible damage caused by the realigned carriageway and are therefore installing a concrete slab across the top of the culvert.

This coming week we will continue the use of the off peak traffic lights to facilitate the culvert protection structure and also to install ducts for electricity cables across the A19

[Subscribe](#)
[Past Issues](#)

Existing pedestrian

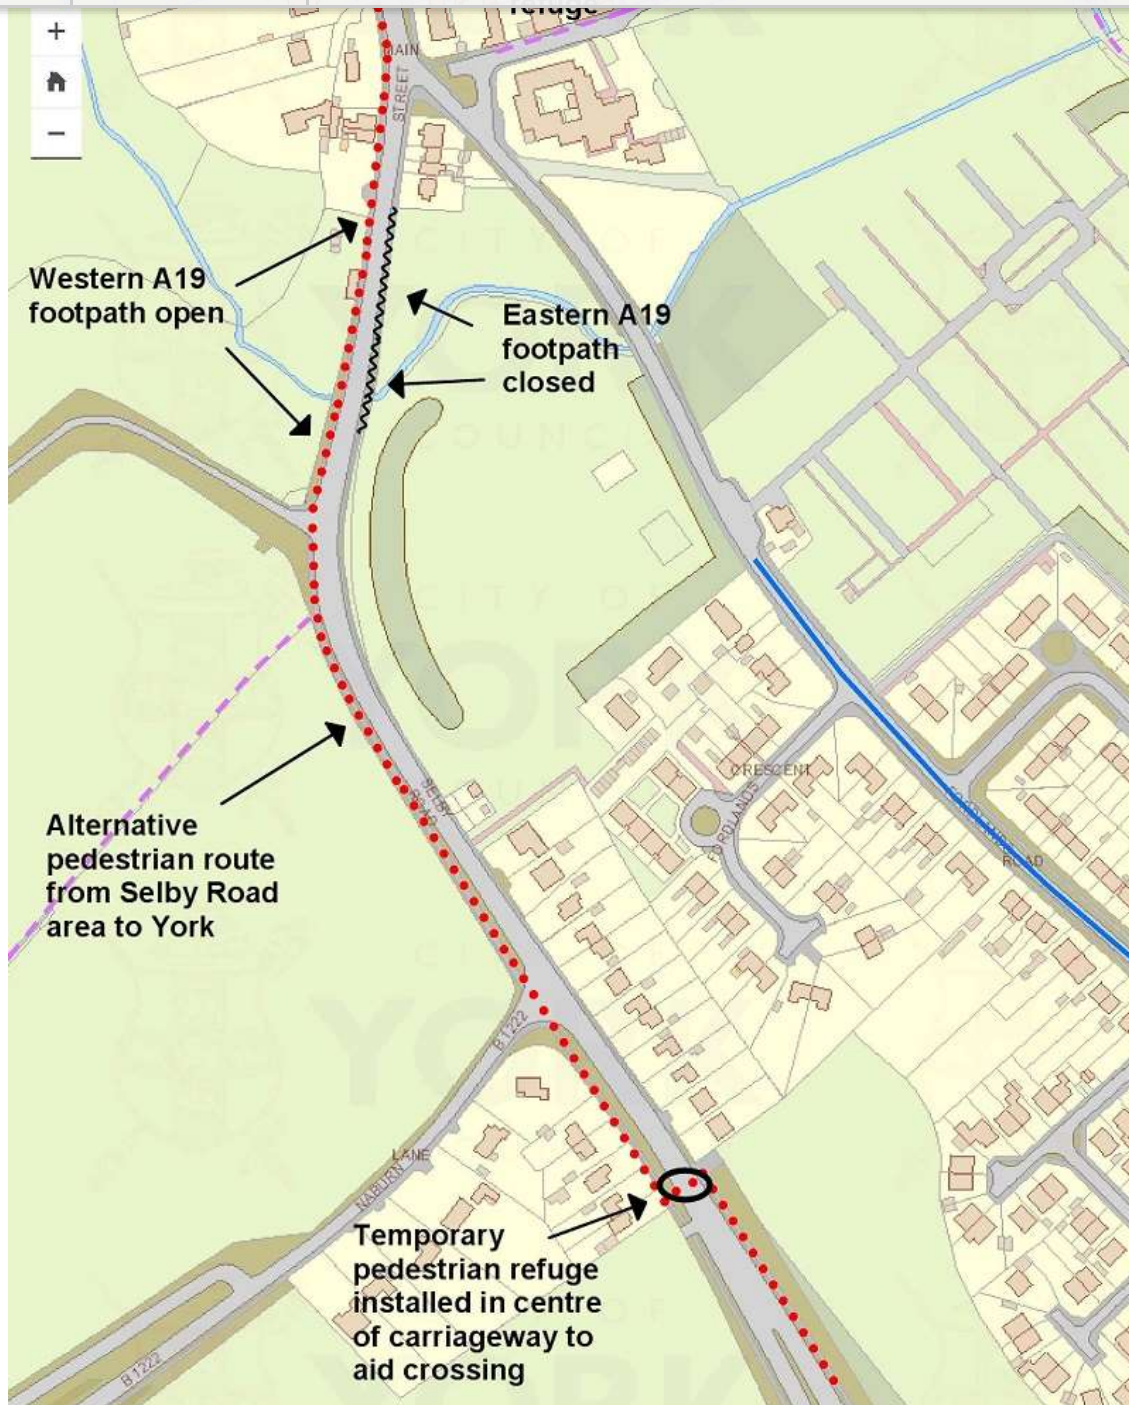

## Safety for children and the wider public.

Please be assured that the different areas of works will be securely fenced at all times to ensure the safety of the public.

We will be receiving deliveries to site this week. Each delivery will be guided into site by one of our employees once traffic and pedestrians are clear from the site entrance. Please be patient if you are held up for a short time whilst these manoeuvres take place.

Pedestrians will be given right of way along the footpaths of Fordlands Road but please be aware of deliveries using the entrances to site off Fordlands Road on occasion.

**Subscribe**

**Past Issues**

Previous editions of our newsletters can be accessed on our website [here](#)

*Copyright © 2018 Howard Civil Engineering, All rights reserved.*

Want to change how you receive these emails?  
You can [update your preferences](#) or [unsubscribe from this list](#)

The MailChimp logo is centered within a dark grey rounded rectangular box. The text "MailChimp" is written in a white, cursive script font.
